Bournemouth University

Heat Decarbonisation Plan

Full Plan

March2023

Version 1 ² Approved by EDC 20.3.23 and CECAP Group on 13.3.23

Version 2- Revised numbers from Mitie in Feb 24

Mitie have undertaken site assessments to produce a detailed summary of the opportunities that are available across each campus and recommended a programme to implement this to 2030/31.

The assessments identified a number of key opportunities across the estate to reduce thermal and electrical load, and to decarbonise the heat systems using a combination of air source and ground source heat pumps.

- There are building fabric upgrade opportunities at 7 of the sites, glazing upgrades at Dorset House and cavity wall insulation at Poole House deliver the highest carbon savings
- There are 9 sites with the potential to install solar PV, Dorset House, Christchurch House and Sir Michael Cobham Library provide the best opportunity for onsite generation
- There are opportunities for heat pumps installations at 16 sites, 12 air source and 4 ground source heat pumps. Poole House (GSHP), Fusion Building (ASHP) Poole Gateway Building (GSHP), Bournemouth Gateway Building (ASHP) and Sir Michael Cobham Library (ASHP) provide the greatest opportunities for heat decarbonisation.
- This report excludes EBC, Student Village, Tolpuddle Annexes, Drewitts Industrial Unit and Wallisdown Playing Fields.

It is estimated that implementation of all identified projects would cost in the region of £21.8m this equates to an average capital spend of £1.3M per annum. The initiatives are estimated to deliver annual cost savings of £454k per annum.

	CAPEX (£)	Cost Savings (£	Scope 1 Emissions (tCO2e)	Scope 2 Emissions (tCO2e)

2026	Lansdowne - The Old Fire Station	Air Source Heat Pump & Fabric Upgrades
	Talbot Campus - Talbot House	Air Source Heat Pump
	Yeovil - University Centre Yeovil	PV
2027	Lansdowne - Studland House	Air Source Heat Pump
	Talbot Campus - Talbot House	PV & Fabric Upgrades
2028	Yeovil - University Centre Yeovil	Air Source Heat Pump
2029	Talbot Campus - Poole House	Ground Source Heat Pump
	Talbot Campus - Student Centre	Air Source Heat Pump
2030	Lansdowne - BGB Talbot Campus - Fusion Building	Air Source Heat Pump
	Talbot Campus - Christchurch House	Ground Source Heat Pump and PV
	Talbot Campus - Poole Gateway Building Talbot Campus - Weymouth House	Ground Source Heat Pump

Carbon Emissions 23
Existing Heating System 27
Chapel Gate Campus 27
Clubhouse 28
Changing Rooms and Squash Courts 29
Football Club Changing Rooms 30
* U R X Q G V P D Q · V ... & R P S R X Q G 31
Cricket Pavilion 32
Summer Cricket Pavilion 33
Bournemouth Gateway Building 35
The Old Fire Station 36
Studland House 37
Christchurch House 40
Dorset House 41
Fusion Building 42
Jurassic House 43
Kimmeridge House 44
Poole Gateway Building 45
Poole House 46
Student Centre 47
SMCL 48
Talbot House 49
Weymouth House 50
University Centre Yeovil 53
Thermal Survey Results 54
Introduction 54
Key observations 55
Talbot Campus SMCL 55
Talbot Campus Poole House 56
Talbot Campus Dorset House 57
Chapel Gate Tennis Club 58
Chapel Gate Changing Rooms and Squash Courts 59
Chapel Gate² Sports Campus 60
University Centre, Yeovil 61
Opportunities 62
Electrical Load Capacity 64
Decarbonisation Opportunities 66
Clubhouse 68
Changing Rooms and Squash Courts 69

Introduction

The Low Carbon Skills Fund (LCSF) enables public sector organisations to DFFHVV IXQGLQJ WR KHOS WKHP GHYHORS D +HDW with the intent of identifying opportunities and pathways in which they can decarbonise their estate.

In 2019 Bournemouth University (BU) made a commitment to achieving Net Zero Greenhouse Gas Emissions by 2030/31 in its Climate and Ecological Crisis Action Plan (CECAP). This represents a further 50% reduction in emissions across all areas of activity.

This builds on success to date where since 2005 BU has reduced its carbon footprint by over 45% through estate and infrastructure investments, as well as by the decarbonisation of the UK national grid. They have installed over 2000 solar panels across Talbot and Lansdowne Campuses, built four new buildings to BREEAM Excellent with a range of low carbon technology including GSHPs and ASHPs. They operate a Building Management System to enable close control of building HVAC and operate a combined Energy and Environmental Management System certified to ISO 140001 and ISO 50001. Their approach extends to the education provided to achieve 88% alignment of curriculum with one or more of the United Nations Sustainable Development Goals.

What is Net Zero?

´1HW =HURµ PHDQV DFKLHYLQJ D EDODQFH EHWZHHQ WKH atmosphere and those taken out.

Carbon dioxide (CO2), a greenhouse gas (GHG), is released when carbon based fuels are burned in homes, buildings, power stations and vehicles. Greenhouse gases absorb and emit UDGLDQW HQHUJ\ ZLWKLQ WKH WKHUPDO infrared radiation to trap heat that would otherwise be emitted out into space. The primary greenhouse gases are water vapour, carbon dioxide, methane, nitrous oxide, and ozone.

Greenhouse gases are a vital part of maintaining life on Earth but have, in recent years, reached levels where an excess of heat is being trapped causing global temperatures to rise. The effect of this temperature increase has dire consequences such as:

Primary impacts:

N

Project Overview

Purpose

This report has been produced to identify the opportunities across the BU estate to transition away from fossil fuels as a source of heat to electrically derived heat, namely through the replacement of gas fired boiler plant with electrically driven heat pumps. The scope of this report is to quantify the energy saving and decarbonisation opportunities associated with this initiative, as well as provide a high level strategy and practical timeline to remove scope 1 fossil fuel emissions across the estate in line with the 8 Q L Y H U V L W \ · V target of 2030/31.

Scope

For the purposes of this report, we are considering Scope 1 and 2 emissions from the following four campuses:

1. Chapel Gate Sports Facility – Christchurch, Dorset, BH23 6BL
2. Lansdowne Campus - 12 Christchurch Rd, Boscombe, Bournemouth, BH1 3NA
3. Talbot Campus – Fern Barrow, Poole, BH12 5BB
4. Yeovil Campus - 91 Preston Road, Yeovil, Somerset, BA20 2DN

Across these four campuses a total of 21 buildings have been selected for this study

The assessment focuses on operational carbon emissions associated with building energy use across the estate

Scope 1 emissions are direct emissions that result from activities owned or controlled by BU which release emissions straight into the atmosphere. This includes all the fuels directly burned in university, owned vehicles and boilers and emissions due to leaks of gases which cause climate change from air-conditioning units

Scope 2 emissions are indirect H P L V V L R Q V U H V X O W L Q J I U R P W K H 8 Q L Y H U V L S X U F K D V H G H O H F W U L F L W \ D Q G K H D W 7 K H V H D U H H P L V V L R Q V sources not owned or controlled by the University. This includes all the electricity that the University purchases. This also includes any heat that is purchased through the district heating scheme

In scope and out of scope activities are listed below:

Scope	Source	Activity	In Scope
1	Stationary Combustion Emissions	Natural gas used for space heating and hot water	Yes
		Liquefied petroleum gas (LPG) used for space heati	Yes

The Talbot campus is the largest of the four campuses assessed and consists of 11 buildings, Z L W K G L V S O D \ H Q H U J \ F H U W L I L F D W H V U D Q J L Q J I U R P D % energy performance operational rating efficiency is typical to good. These reflect the q W* n BT 1 g /TT0



Campus	Building	Annual Electricity Consumption	Annual Natural Gas Consumption	Annual LPG Consumption	Annual Biomass Consumption	Electrical Intensity (kWh/m2)	Thermal Intensity (kWh/m2)
Chapel Gate	Changing Rooms and Squash Courts	90,865	0	143,894	0	106	168
	Clubhouse	131,273	0	207,885	0	106	168
	Cricket Pavilion	28,561	0	0	0	106	0
	Football Club Changing Rooms	8,674	0	0	0	106	0
	* U R X Q G V P D Q · V &	3,385	0	0	0	106	0
	Summer Cricket Pavilion	0	0	0	0	0	0
Lansdowne	Bournemouth Gateway Building	1,190,983	557,643	0	0	115	54
	The Old Fire Station	167,099	124,314	0	0	98	73
	Studland House	592,062	192,275	0	0	99	32
	Christchurch House	428,140	295,724	0	0	83	58
Talbot							

Table 6. Energy Profile by site

The chart below illustrates the annual energy consumption on a building by building level. Poole House is clearly the largest consumer overall which is of no surprise given its large floor area. Bournemouth Gateway Building has a large electrical consumption compared to its natural gas consumption; this is likely due to the electrical demand required for the heat pumps

Annual energy consumption across in -scope portfolio (kWh)

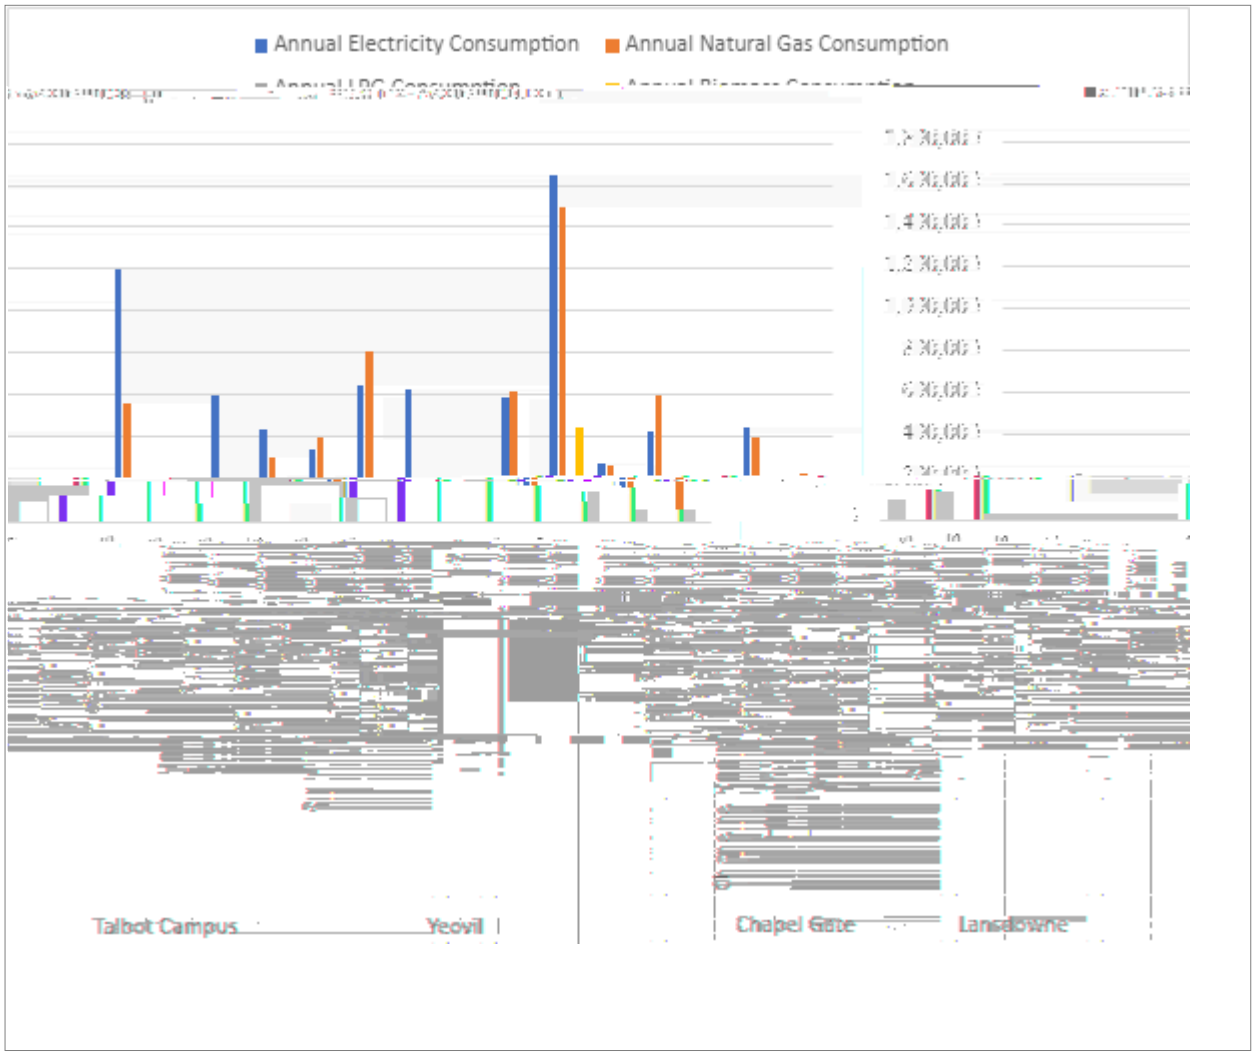

Despite having a large energy consumption, the energy intensity of Poole House is relatively low. Jurassic House, however, has an extremely intensive electrical demand due to the data centre and cooling plant located within

Annual energy intensity across in-scope portfolio (kWh)

7 K H P R G H O O H G W U D M H F W R U \ K L J K O L J K W V W K D W W K H F D U E R Q L V H G L Q W H Q V L W \ R I W K H J U L G H O H F W U L F L W \ U H S U H V H Q W H G E \ W

Clubhouse

Building	Floor Area	DEC Rating
Clubhouse	859	F

Description of building services

The Clubhouse is a two storey building, with a flat and nursery operating on the 1st floor and the ground floor comprising of catering and social facilities. The main bar area is glazed with full height, openable doors. The construction of the site is cavity wall, and due to the age of the building it is assumed that this is insulated as no evidence of drilling could be found. Heating is provided by a Remeha 360 LPG boiler which feeds three CT circuits which in turn supply a variety of LTHW radiators, most of which were fitted with TRVs. The boiler also feeds a 208 litre Gledhill calorifier for DHW, which has a 3kW version element for backup. LPG is also used in the catering facilities. LPG and electricity are metered at a cam level, and so have been apportioned across buildings on a kWh/m2 basis

Energy Analysis

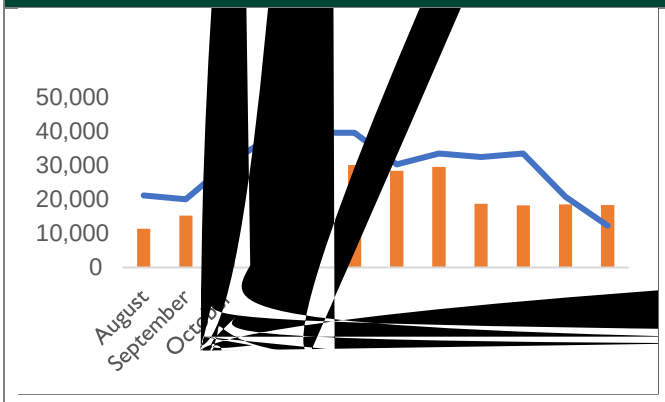

Photos

Football Club Changing Rooms

Building	Floor Area	DEC Rating
Football Club Changing Rooms	270	N/A
Description of building services		

The football club changing rooms are located away from the main

* U R X Q G V C E P D Q Y

Building	Floor Area	DEC Rating
* U R X Q G P D Q u n d	82	N/A
Description of building services		

This34 0.48 0.48 09.76 2re f* 34* n84nal76 2re Q q 446 (i Q qngl]TJ ET 76 2r 44* ntoic)-

Cricket Pavilion

Building	Floor Area	DEC Rating
Cricket Pavilion	32	N/A
Description of building services		

The cricket pavilion is a single storey structure containing a small bar, social area, kitchenette and changing facilities. Heating throughout is provided by wall mounted panel radiators, with DHW pro by point of use generators. There are several electrical showers in the changing areas. There is d

Lansdowne

The Old Fire Station

Building	Floor Area	DEC Rating
The Old Fire Station	1,706	C

Description of building services

The Old Fire Station building is a entertainment venue complete with offices on the top floor. Heating is pro by a combination of LTHW natural gas boilers as well as various split units across the site. The boilers have recently been replaced in the basement plantroom with three Vaillant EcoTech VU1006 units rated at 100kW each. These feed a VT circuit for the radiators, a CT circuit for the AHUs and the DHW. The DHW system h been upgraded from a storage calorifier, to a PHEx system provided hot water at 62degC.

The building is solid wall construction and there are limited opportunities to improve the building fabric for conservation reasons. One of the main benefits that could be introduced, is upgrading the existing doors to more suitable option which would reduce thermal loss through insultation and more importantly, reduced air infiltration. There is no opportunity to install solar PV for the reasons above.

Studland House

Building	Floor Area	DEC Rating
Studland House	5,133	C

Description of building services

Studland House is split over eleven stories, including the basement and the roof top plant room. One half o building only has 5 stories, including the open ground floor which houses the car park and data centre. The top plant room contains three Ideal Evomax boilers rated at 100kW each. These supply a CT circuit which fe some radiators, trench heating and an AHU in the basement, as well as a VT circuit. The VT circuit has bee modified to supply that radiators on a zoned basis, with floors 5, 6, 7 and 8 being controlled together, floor 4 havi controls for the front and back halves of the building, and each floor below having individual control. The ma heat emitters are radiators which are fitted with TRVs throughout. There is a large data centre located on the ground floor which could act as a heat source.

DHW is provided through point of use electrical heaters with 1 to 2 located per floor. The site also has a substantial PV array installed on the roof.

Energy Analysis

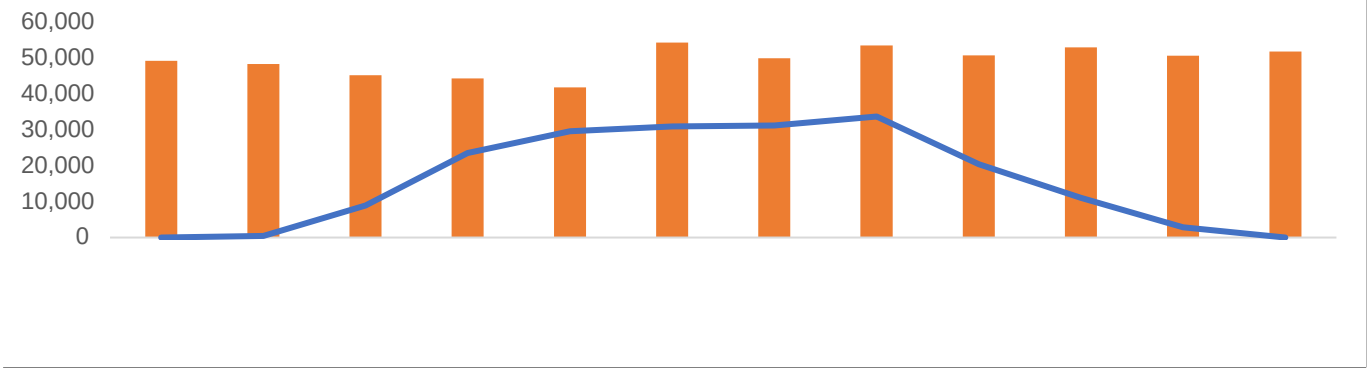

Photos

Talbot Campus

Talbot Campus is located near the centre of Bournemouth, and comprises 13 buildings spread over a pedestrianised site. There are various ages of buildings ranging from Poole House which was originally

Site	Primary Heating Source	Remaining Life (Years)	Condition

ChristchurchHouse

Building	Floor Area	DEC Rating
ChristchurchHouse	5,133	C

Description of building services

Kimmeridge House

Building	Floor Area	DEC Rating
Kimmeridge House	1,541	D

Description of building services

Kimmeridge House is a teaching space constructed in 2003. It contains three lecture theatres and two semi
rooms over two storeys, with a high ground floor to accommodate the lecture theatres, and an open plan fo
utilising air curtains to reduce therml loss.

The plant room is located in the roof void and contains an air handling unit, the boilers, a DHW cyli
and the associated pump sets. Further plant is located externally, with two additional air handling u
and a chiller. The boilers are Hamworthy Purewell Classics with a combined maximum output of 285k
They are designed to supply two CT circuits, and one VT circuit which feed a combination of radiat
AHU coils and underfloor heating. The boilers also feed a DHW calorifier, however this is switched
to immersion heaters in the summer months to reduce gas consumption.

Energy Analysis

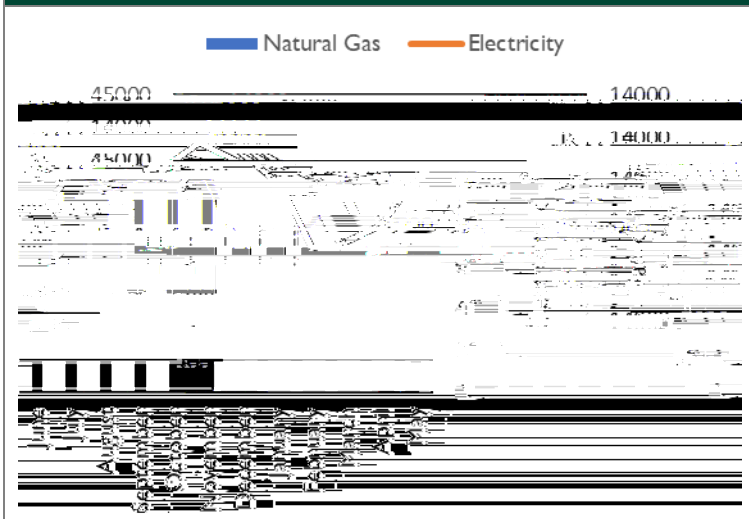

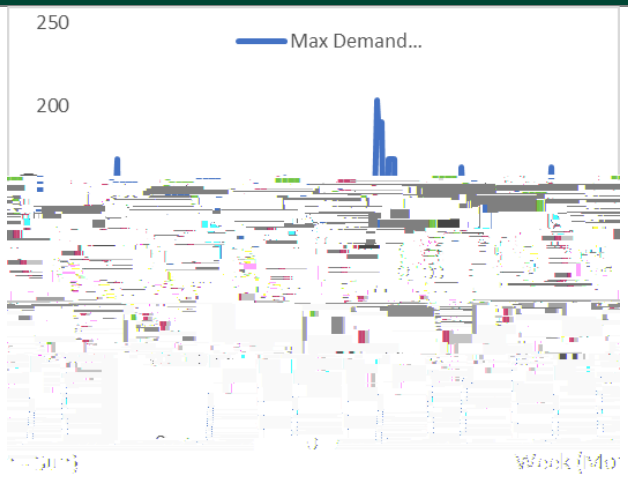

Photos





Poole Gateway Building

Building	Floor Area	DEC Rating
Poole Gateway Building	6,790	D
Description of building services		

Poole House

Building	Floor Area	DEC Rating
Poole House	18,628	D

Description of building services

Poole House consists of an original 6 storey tower dating from the 1970's, which was expanded with a sing storey extension to provide a catering college. The tower has a small gas boiler which serves a small numb radiators, but the majority of the heating load is served via natural gas boilers and a biomass boiler. The boile new and consist of a 750kW modular Ideal OvoMod system, as well as a 500kW Binder biomass boiler. Th boilers feed a header which in turn supplies a number of CT and VCT units across the catering and teaching facilities, as well as a domestic hot water supply. The DHW is primarily supplied by a PHEx connected to th header, however there is also solar thermal that supplements the demand.

The site has a number of solar PV installations which is currently being expanded. There is the opportunity improve the building fabric in approximately 50% of the structure.

Energy Analysis

Photos

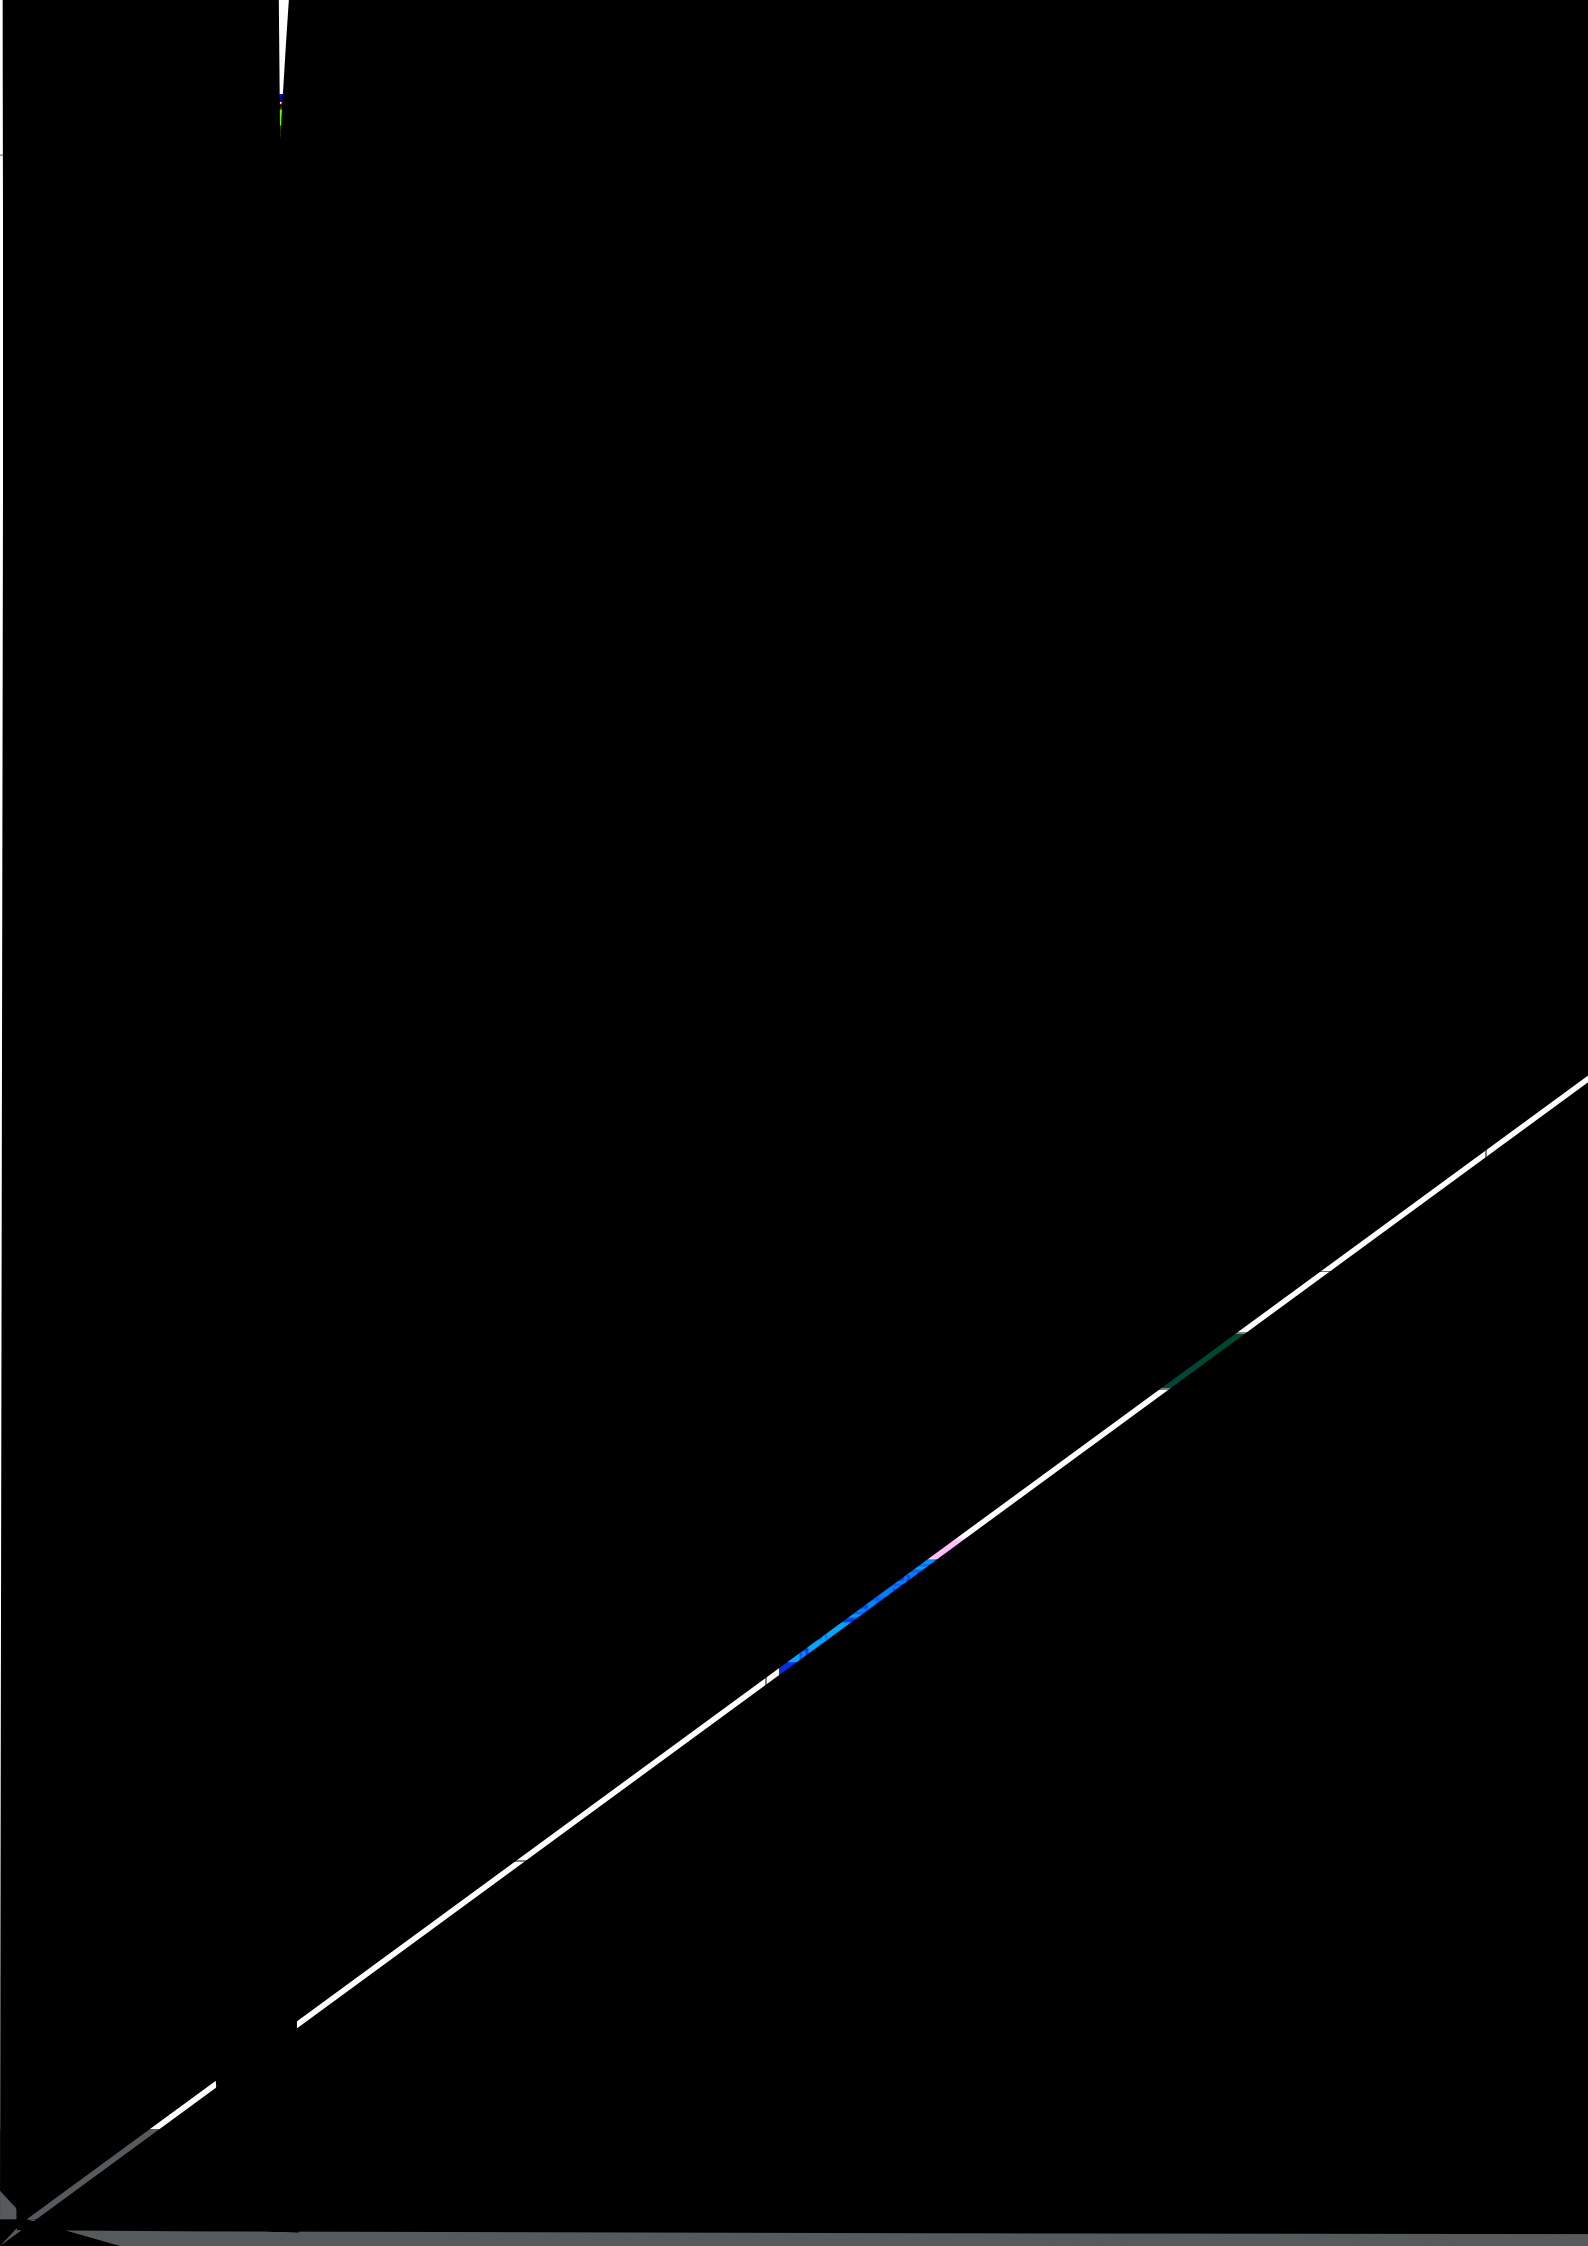

SMCL

Building	Floor Area	DEC Rating
SMCL	6,117	B
Description of building services		

SMCL (Sir Michael Cobham Library) is a student library that is split into two connected spaces: Main and The Main was part of the original construction in 1987 and is a two-storey space of cavity wall construction an a flat roof. It comprises of open plan space study areas, as well as breakout rooms and several staff offices on t ground floor.

The Tower is a modern addition added in 2002 and comprises of open plan study areas over 5 storeys ar connected to the open study spaces of the Main on the ground and 1st floors. The Tower is connected via unheated walkway to a separate building and also houses a café which is sub-metered from the main supply and has no gas consumption. There are two separate plantrooms for the Main and the Tower, each with separa mechanical distribution systems. In addition to this, both the Main and the Tower have separate LV supplies.

The Main is primarily heated from a plant room that is accessed externally. There are two Hamworthy We 200 natural gas boilers that feed a LTHW system that supplies three circuits. The tower plant room contai three Hamworthy Purewell 95 boilers with a combined maximum output of 285kW. These feed VT and CT circuits, as well as an AHU heating coil located in the same plant room.

Talbot House



Yeovil

University Centre, Yeovil, is a single building which acts as an education centre and regional hub for students o
placements throughout the South West.

University Centre Yeovil

Building	Floor Area	DEC Rating
University Centre Yeovil	2,179	B

Description of building services

University Centre Yeovil is an owned building split into two parts connected by a link corridor. The original construction is a two storey, heavily glazed unit which houses lecture facilities and IT rooms. This section is using three Hamworthy Purewell 95 boilers which feed three VT circuits (North, South and Ground) to supply heating via radiators. Flow and return temperatures of 74degC and 50degC were observed. Domestic hot w provided by immersion elements in calorifiers, or by point of use generation. There is a significant opportuni upgrade the glazing in this site to not only reduce thermal loss, but also thermal gain in summer.

The extension is a more modern construction and is heated using a Vaillant EcoTech 637 gas boiler, alongs number of split units and electrical radiators. There is an opportunity to install a 35kWp solar PV system on this site.

Energy Analysis

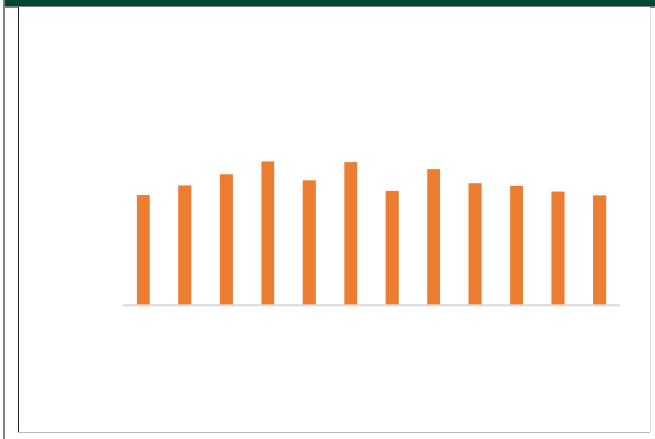

Photos

Key observations

Talbot Campus - SMCL

- The roof appears to be in good condition, with a uniform temperature observed
- The biggest concern with this building is the glazing on the original construction. These appear to have varying levels of performance with some showing temperatures of ~15degC indicating poor installation or air leakage
- On all elevations, there is evidence of a thermal leak between the roof joins including the crown on top of the tower

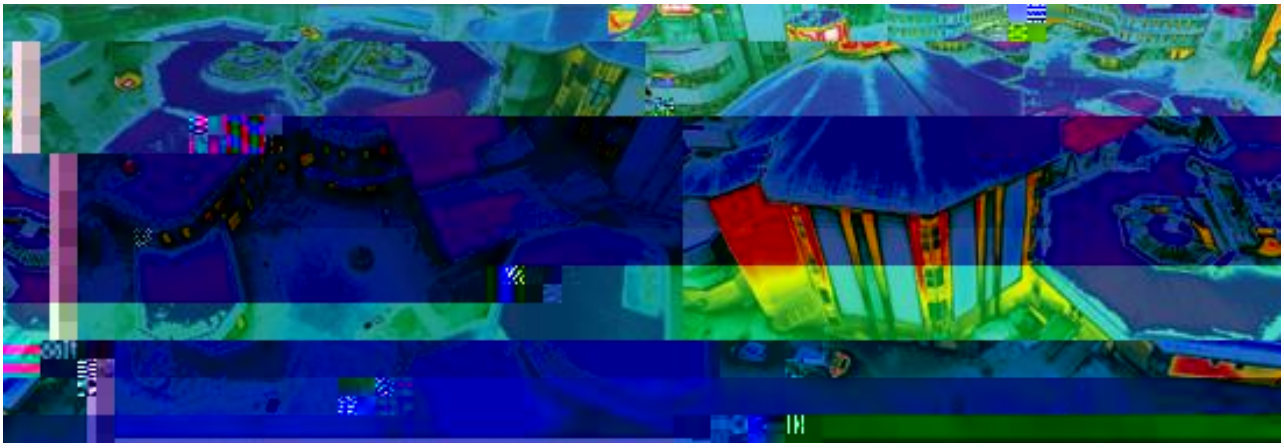

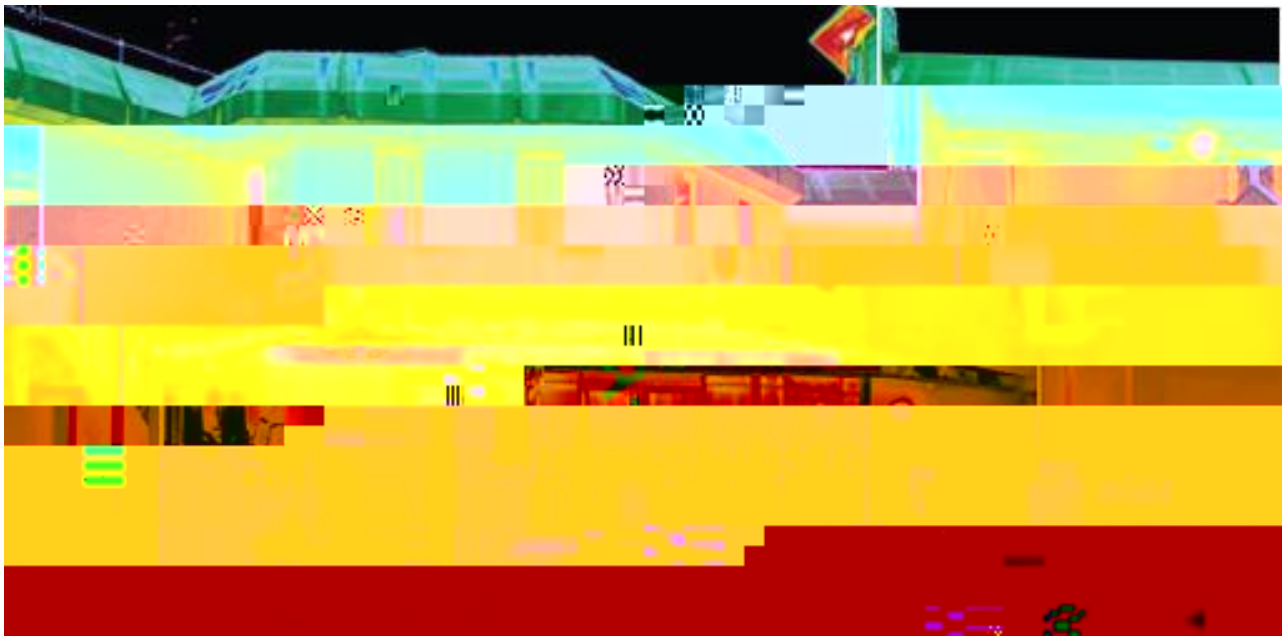

Talbot Campus - Poole House

- The roof appears to be in good condition, with a uniform temperature observed
- The southern elevation (by the Estates Reception) appears to either be missing insulation, or installed insulation has degraded significantly
- The glazing across this building is mixed, with some performing as expected and others performing very poorly

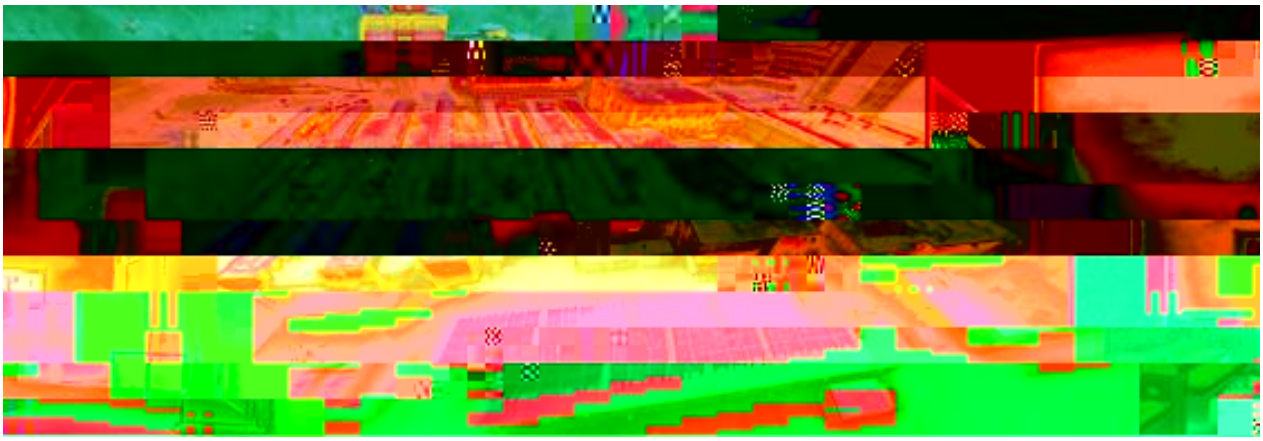

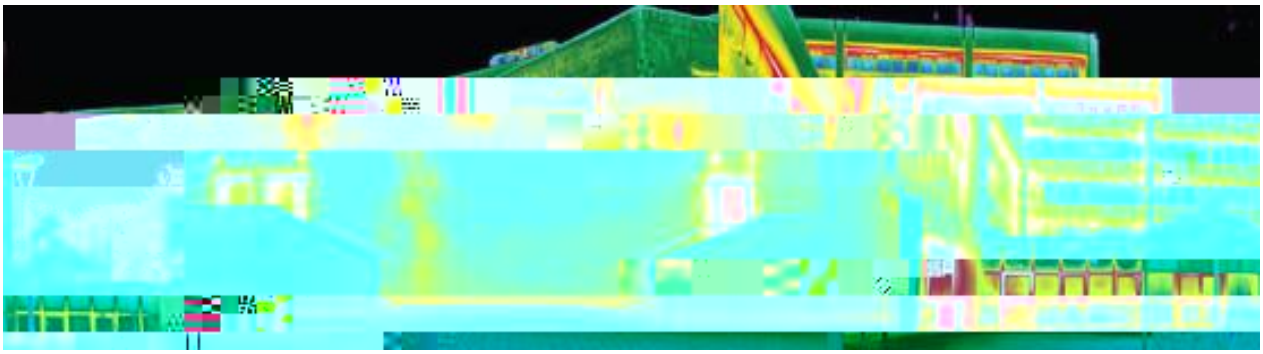

Talbot Campus Dorset House

- The windows, and especially their frames, are operating poorly which may be due to aging assets or poor installation W K D W K D V Q thHermal Performance L V H G
- There is a clear difference between the ground floors and the upper two stories, with the ground floor leaking considerable amounts of heat
- The roof covering looks good, with little to no signs of thermal bridging

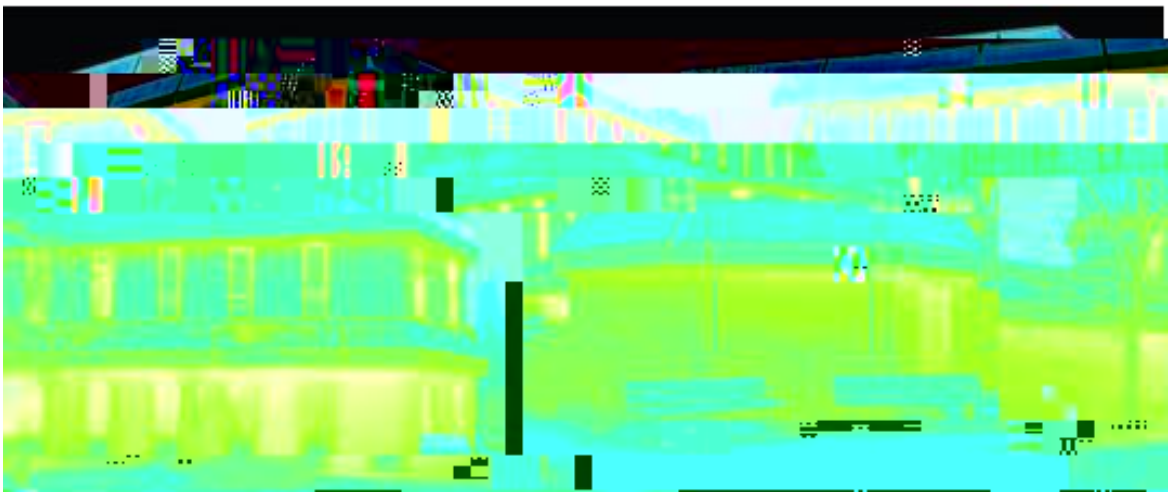

Chapel Gate - Tennis Club

- There are good even temperatures across some of the elevations suggesting that the insulation is performing well
- Minor areas of heat loss noted at the roof line.
- The temperature across the south elevation appears high further investigation is recommended in this area to ascertain insulation levels or other factors

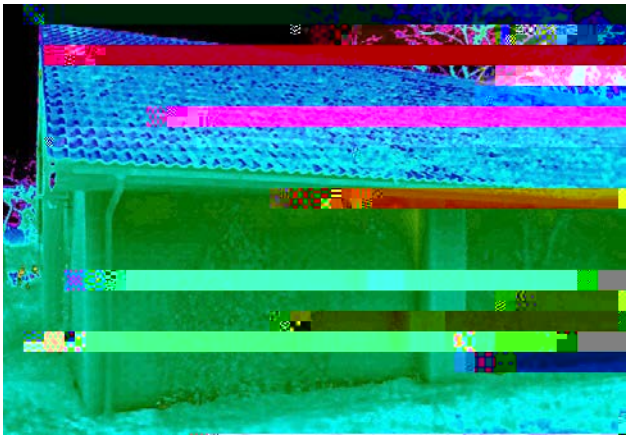
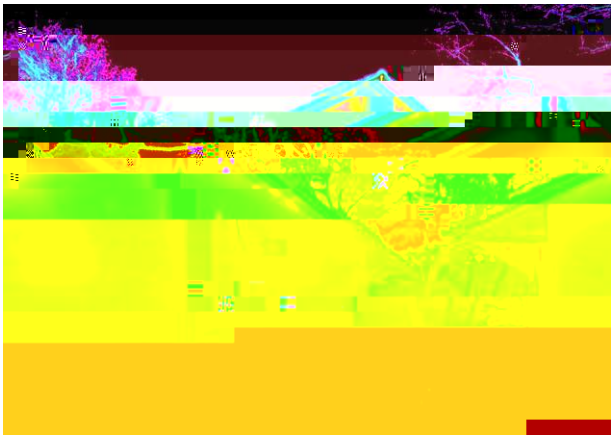
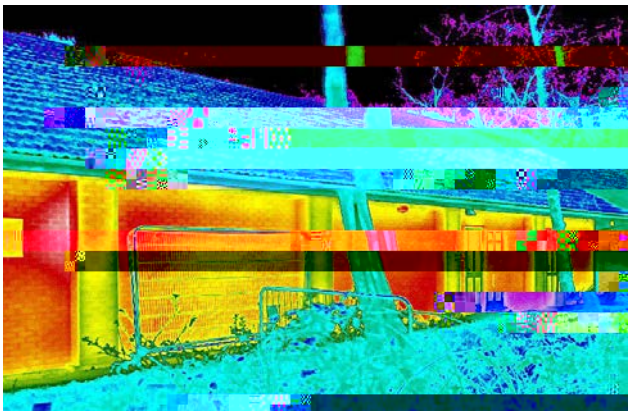
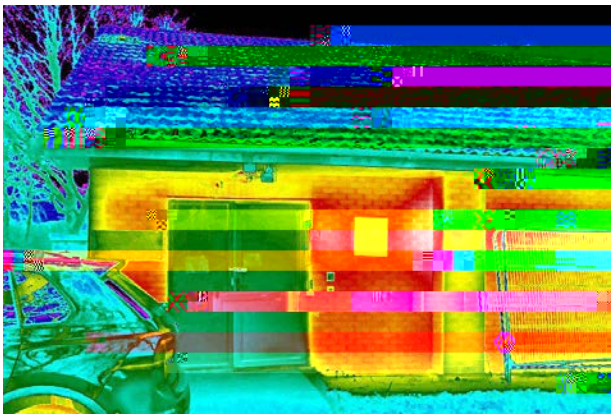

Chapel Gate² Sports Campus

- Overall, the roof and elevations show an even colour and temperature distribution, suggesting very little heat loss
- The windows, and especially their frames, are operating very poorly which indicating aging assets or poor installation not prioritising thermal performance
- The red vented areas should be investigated further for missing or misaligned insulation
- Insulation is performing poorly on both walls of the south elevation, it appears to have little or no insulation
- The door appears to be performing poorly, this should be investigated further as it was in constant use at the time of the survey

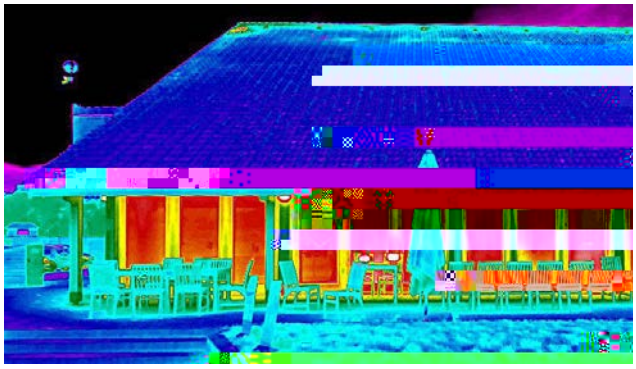

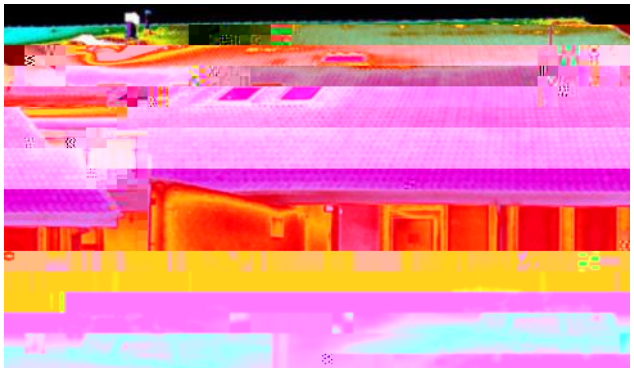

There are multiple technologies that exist that could be used to decarbonise the heat demand, however several have been discounted for the reasons below

Solar Thermal – high capital cost, using space that would be better suited to solar PV

Hydrogen – Uncertainty over zero carbon credentials and not a mature technology

Biomass – high operating costs, issues with resilience and Scope 1 emissions

Direct electric – very high operating costs, requiring a large electrical connection

District Heat Networks – Carbon savings are dependant on the input heat generation, usually a CHP and gas boilers.

Campus	Site	Site Capacity (kW)	Confirmation	Electrical capacity needed (kW)	Existing peak demand (kW)	Sufficient Capacity
Chapel Gate	Clubhouse	199	Confirmed	40	155	NO
	Changing Rooms and Squash Courts			48		

Changing Rooms and Squash Courts

Building
Changing Rooms and Squash Courts

Technological Solution
This building could be served using electrical panel radiators or similar, however the greatest carbon b and efficiency gains would be from a heat pump. An air source heat pump would be the recommended technology due to the relatively small size of the heating capacity which negates the need for investme ground source heat pump. The preferred solution would be one combined heating system that serves the Clubhouse and the Changing Rooms/Squash Courts. The recommended date for install has been sugg 2025 due to the age of the boilers, and the relatively simple installation. In addition to these measures, cavity wall insulation is also recommended.

Recommended Decarbonisation Options

Technology	CAPEX (£)	OPEX Saving (£)	Scope 1 Savings (tCO2e)	Scope 2 Savings (tCO2e)	Proposed Installation Date
Baseline	£-	£79,754	44.6	26.2	Baseline
Cavity Wall Insulation	£49,100	£803	1.1	0.0	2024
Solar PV	£42,353	£11,753			

Lansdowne

Bournemouth Gateway Building

Building
Bournemouth Gateway Building
Technological Solution
As BGB is a modern construction, already with a GSHP, the combined carbon emissions associated with the heating are relatively low despite using natural gas for part of the heating and hot water. It would be recommended that a new air source heat pump system would be installed, which would act as a reserve t existing GSHP when peak heating levels are required Due to the age of the building and the low carbon emissions, it is recommended that this system is installe the end of the programme in 2030, which will allow the university to benefit from the installed assets
Recommended Decarbonisation Options

Technology	CAPEX (£)	OPEX Saving (£)

Studland House

Building
Studland House
Technological Solution

Due to the size of the required heat pump and the location of the building, a ground source heat pump

Talbot Campus

ChristchurchHouse

Building
Christchurch House

Technological Solution
Whilst Christchurch House on it's own would justify an air source heat pump installation due to it's size a heat demand, there is an option, however, to link several buildings together and form a small communal heating system. The scope of this would require further consideration, however one proposal could be an ambient loop taking waste heat from Jurassic House and smaller water source heat pumps at a building to boost the temperature. The proposed date for installation is 2030 due to the complex design requirements and the required grou works.

Recommended Decarbonisation Options

Technology	CAPEX (£)	OPEX Saving (£)	Scope 1 Savings (tCO2e)	Scope 2 Savings (tCO2e)	Proposed Installation Date
Baseline	£-	£195,377	54.0	85.6	
Solar PV	£105,882	£29,382	0.0	15.9	2030
Ambient heating loop with Weymouth, PGB and Jurassic.	£1,732,501	£13,519	54.0	-12.7	2030
Total	£1,838,383	£42,901	54.0	3.2	

Pathway Comparison

Dorset House

Building
Dorset House
Technological Solution

Fusion Building

Building
Fusion Building
Technological Solution
The Fusion House boilers could be replaced with a high temperature heat pump, which could serve the demands of the high grade header (DHW and radiators). This may be via an ASHP or a WSHP fed from a new communal system, but extending the GSHP array of boreholes wouldn't be recommended as a retro solution. Timing has been proposed as 2030 as the building already has a low carbon intensity for it's heating, and the existing assets are new
Recommended Decarbonisation Options

Kimmeridge House

Building
Kimmeridge House
Technological Solution

Poole Gateway Building

Building
Poole Gateway Building
Technological Solution

PooleHouse

Building
Poole House
Technological Solution
PooleHouse is a considerable heating load, and due to the recent installation of the gas boilers and the a the biomass boilers (10years) it is recommended that any transition to a low carbon heating system is ca out towards the end of the 2030 target. Due to the size of the heating demand, it is recommended that a ground source heat pump is explored as this will maximise the COP of the system whilst negating some issues with amending a complicated, old heating system to accept a lower flow temperature. There are several areas that would benefit from cavity wall insulation to reduce thermal loss

Recommended Decarbonisation Options

Technology	CAPEX (£)	OPEX Saving (£)

StudentCentre

Building
Student Centre
Technological Solution

SMCL

Building
SMCL
Technological Solution
SMCL has already had an Air Source Heat Pump project put forward for the Public Sector Decarbonisat Scheme with the aim of securing grant funding. If successful this will require delivery by March 2024. Solar PV, double glazing and cavity wall insulation were also recommended however it was decided to keep these measures separate to the grant application .
Recommended Decarbonisation Options

Technology	CAPEX (£)	OPEX Saving (£)	Scope 1 Savings (tCO2e)	Scope 2 Savings (tCO2e)	Proposed Installation

Weymouth House

Building
Weymouth House
Technological Solution

Yeovil Campus

Key Recommendations

The site assessments have identified that the following interventions could be made at each site:

Capital Projects Carbon Savings (tCO2e Scope 1 & 2)								
Campus	Building	Cavity Walls Insulation	Heat Reutilisation	Glazing Upgrade	Solar PV	ASHP	GSHP/ Ambient Loop	Total



Year	Site	Measure
2023	Chapel Gate - Changing Rooms and Squash Cou	Building Fabric Upgrades
2024		

Delivery Plan

Through analysing the findings from the site assessment and aligning recommendations with the estates boiler lifecycle replacement plan it is also possible to create a capital projects pipeline for the proposed initiatives. It is estimated that this will involve around £21.8m of project works. Around 90% (£19.7m) of capital project cost is associated with the replacement of boilers with heat pumps, 3% (£528k) relates to building fabric upgrades, with the remaining 2% (£554k) relating to Solar PV.

Capital Projects Cost (£k ex VAT)										
Campus	Building	2023	2024	2025	2026	2027	2028	2029	2030	Total

Student	£551k
Centre	ASHP

Challenges

There will be a number of challenges associated with delivering this heat decarbonisation plan and achieving net zero carbon across the estate:

Capital Expenditure and Funding

A key challenge will be sourcing and signing off on the significant capital sums required to replace the existing plant as the installation of heat pump technology will be significantly more expensive than like for like replacement.

In total a budget of £21.8m will be required, which will need to be earmarked for low carbon projects. Individual projects will range in cost from £35k – £3.5m and therefore these will require different levels of approval, budgeting and funding routes The HDP estimated budget to 2030 will inform the EDF3 decarbonisation budget.

If additional financial resources are required for delivery in excess of the normal cycle of capital expenditure, this could be met through a combination of savings from the implementation of energy saving projects or pursuing grant funding from external sources, such as the Public Sector Decarbonisation Scheme.

Funding is available to support with delivery as highlighted in the Funding Routes and Procurement Options section. However commercial risks will need to be reviewed if considering third party funding; an eligibility and availability review will be advised if considering public funding to guarantee chances of application success.

A challenge for BU is that many of the buildings still have useable gas boilers with 10 years of life remaining making them less suitable for obtaining external funding through opportunities like PSDS. However third party funding may be able to address this challenge.

BU will investigate opportunities to further invest in M&V for the HDP, to accurately understand the quantified savings and deploy early mitigation/ correction to facilitate NZ strategy. A supporting metering strategy will also need to be in place to monitor operational performance. A review of operational changes as a result of implementing HDP is also required to understand the operational impact i.e., additional maintenance costs. Finally, campus behavioural training and energy awareness will also be implemented to ensure the buildings and new assets are managed as efficiently as possible

Grid Constraints

The success of this plan will be defined by the ability to increase energy capacity onsite. It is expected that in order to deliver this plan, grid infrastructure upgrades will be required at sites lacking a medium voltage supply. This will need to accommodate plans for other projects; EV charging, solar PV and data centres as examples. Additional project works and cost incursions will be required to increase this with the DNO if sites wish to increase G H P D Q G 6 L W H · V Z L O O W K H U H I R U H E H V W D Q G D U G L W L R Q D O W L P H D Q G F R V W L Q F X U V L R Q V W R G H O L Y H U W K L V assessment to fully understand feasibility and liability challenges.

Governance

Each campus has been audited by an Energy Solutions Engineer to identify the opportunities available across each building, this is to ensure that proposed solutions can be tailored to H D F K E X L O G L Q J · V U H T X L U H P H Q W D Q G V L W X D W L R Q

The following strategy was applied to each building in sequential order to identify potential measures:

1. Fabric First Approach: Reduce existing thermal demand by improving building fabric, this will reduce heat pump operation costs and could assist with heat pump sizing
2. Renewable Generation: Where viable install Solar PV to part mitigate the expected additional electricity demand associated with heat electrification
3. Heat Electrification: Remove scope 1 fossil fuel emissions by replacing existing fossil fuel fired heating systems with air source heat pumps
4. Offsite Renewables: Ensure that high quality green electricity tariffs are procured to mitigate remaining scope 2 emissions

The audit findings have been developed into a series of recommendations that feed into a projects register for energy efficiency and low carbon transition. These Energy Conservation Measures (ECM) create the basis for the proposed heat decarbonisation strategy. To further this a delivery programme has been designed to ensure that all projects are implemented before the net zero GHG emissions target of 2030/31

It is proposed that all fabric first and renewable generation measures are prioritised and implemented across the estate before or in tandem with heat pump installations. This is U H F R P P H Q G H G D V % R X U Q H P R X W K 8 Q L Y H U V L W \ · V F X U U H Q wholesale market prices; energy conservation measures will reduce exposure to these, additionally high rates can also be capitalised upon to improve the return-on-investment periods. Heat pump installations should occur in line with the existing boiler lifecycle replacement program to ensure that older or inefficient systems are prioritised for replacement.

This assessment has identified a total £21.8M of potential decarbonisation projects, £9.1M of this cost relates to the replacement of boiler systems with air source or ground source heat pumps which will be a key intervention if Bournemouth University wish to remove scope 1 fossil fuel emissions.

Projects	CAPEX (£)	Cost Savings (£	Scope 1 Emissions (tCO2e)	Scope 2 Emissions (tCO2e)
Cavity Wall Insulation	£538,000	£18,187	21.5	0.0
	£990,100			

Solar PV	£554,573	£155,647	0.0	84.1
ASHP	£ 9,825,445	£58,772	665.3	-214.9
GSHP	£9,885,445	£151,877	495.3	-132.7
Total	£21,793,418	£454,467	1226.0	-242.4

More specifically the following key initiatives have been identified:

- There are building fabric upgrade opportunities at 7 of the sites, glazing upgrades at Dorset House and cavity wall insulation at Poole House deliver the highest carbon savings
- There are 9 sites with the potential to install solar PV, Dorset House, Christchurch House and Sir Michael Cobham Library provide the best opportunity for onsite generation
- There are opportunities for heat pumps installations at 16 sites, 12 air source and 4 ground source heat pumps. Poole House (GSHP), Fusion Building (ASHP) Poole Gateway Building (GSHP), Bournemouth Gateway Building (ASHP) and Sir Michael Cobham Library (ASHP) will provide the greatest opportunities for heat decarbonisation.
- This report excludes EBC, Student Village, Tolpuddle Annexes, Drewitts Industrial Unit and Wallisdown Playing Fields.

Through analysing the findings from the site assessment and aligning recommendations with the estates boiler lifecycle replacement plan it is also possible to create a capital projects pipeline for the proposed initiatives. It is expected that the following pipeline of projects will QHHG WR EH LPSOHPHQWHG LQ RUGHU WR GHFDUERQLVH overall emissions:

Term	Description	Definition
Net Zero	Net Zero Carbon	The balancing of amount of emitted greenhouse gases with the equivalent emission Q q 259.85 7

Net Z6704f* 769.44 BT 0.231 0.22 713.02 86.64 41.76 re W* n
